

Annexure- 1

**AUTOMATION OF SOFTWARE PROCESS WORK FLOW DESIGN &
DEVELOPMENT AND MAINTNANCE FOR EMBEDDED AND
SIMULATION PROJECTS**

Sute

Table of Contents

1. Background	4
2. Scope	4
3. Details of Existing Software environment	4
4. Existing Software Architecture	5
5. Features to be implemented in the existing tool	8
5.1. Development of Word equivalent editor and integration with the existing tool 8	
5.2. Development of new workflows for HMI requirement capture	9
5.3. Support and maintenance of the existing work flow	9
5.3.1. Requirement Management Activities	9
5.3.2. Schedule and Activity Management Activities	10
5.3.3. Clear Case Activities	10
5.3.4. RPE Activities	10
5.3.5. User Management Activities	11
5.3.6. Server Activities	11
5.3.7. Backup and Restoration Activities	11
5.3.8. Miscellaneous Activities	11
6. Proposed architecture	12
7. Activities to be carried for new software framework implementation	13
7.1. Design and development of tool with new software framework	13
7.2. Testing and Documentation with new software framework	13
7.3. Migration of the data from the existing to the new software framework .	14
7.4. SCADE and RAPSODY integration	14
7.5. Support and maintenance of the work flow	14

Conte

7.5.1.1. Requirement Management Activities	14
7.5.1.2. Schedule and Activity Management Activities	14
7.5.1.3. ClearCase Activities.....	15
7.5.1.4. RPE Activities	15
7.5.1.5. User Management Activities	16
7.5.1.6. Server Activities	16
7.5.1.7. Backup and Restoration Activities.....	16
7.5.1.8. Miscellaneous Activities.....	16
8. Onsite support	16
9. Material to Be Given by ADA	17
10. Vendor - Pre-requisite Qualification.....	17
11. Technical Team Expertise	18
12. Technical evaluation	19
13. Resource deployment.....	20
14. Training.....	20
15. Handing over activities	20
16. Schedule and Milestone Deliverables.....	21
17. Acceptance criteria	22
18. Terms & Conditions.....	22

Sinte

1. Background

ADA has developed an in-house process work flow tool based on DO-2167A which is being used for embedded and simulated software development. The main features of the work flow namely Requirements management, Task Scheduling, Activity tracking and management, Report generation, User management etc are used by approx. 50 users across multiple projects. The work flow tool is integrated with Clear case for Configuration control and Rational Publishing Engine (RPE) for the report generation.

In order to automate the development and up-gradation for meeting DO-178 guidelines, the developed work flow software needs following features which needs to be integrated with existing tool:

- a. Development of Word equivalent editor and integration with the existing tool
- b. Development of new workflows for HMI requirement capture
- c. Support and maintenance of the work flow

Also to address the tool obsolescence the entire tool needs to be migrated to the new software framework and the following enhancements are further planned.

- a. SCADE and RAPSODY integration
- b. Support and maintenance of the work flow

2. Scope

The scope of the vendor is to carry out the work flow development and migration activities detailed in this document. The vendor shall deploy resources at ADA / vendor's site to carry out these activities. However the maintenance and integration activities need to be carried out by resident resources deployed by vendor at ADA. The details are given below


3. Details of Existing Software environment

The details of the development environment of the existing tool are as follows:

Front End: PHP with HTML CSS ,JavaScript, JQuery, AJAX, C#
Back End:PHP
Framework: Yii2
Database: MySQL
IDE: Visual studio code

4. Existing Software Architecture


The existing software architecture is given below:

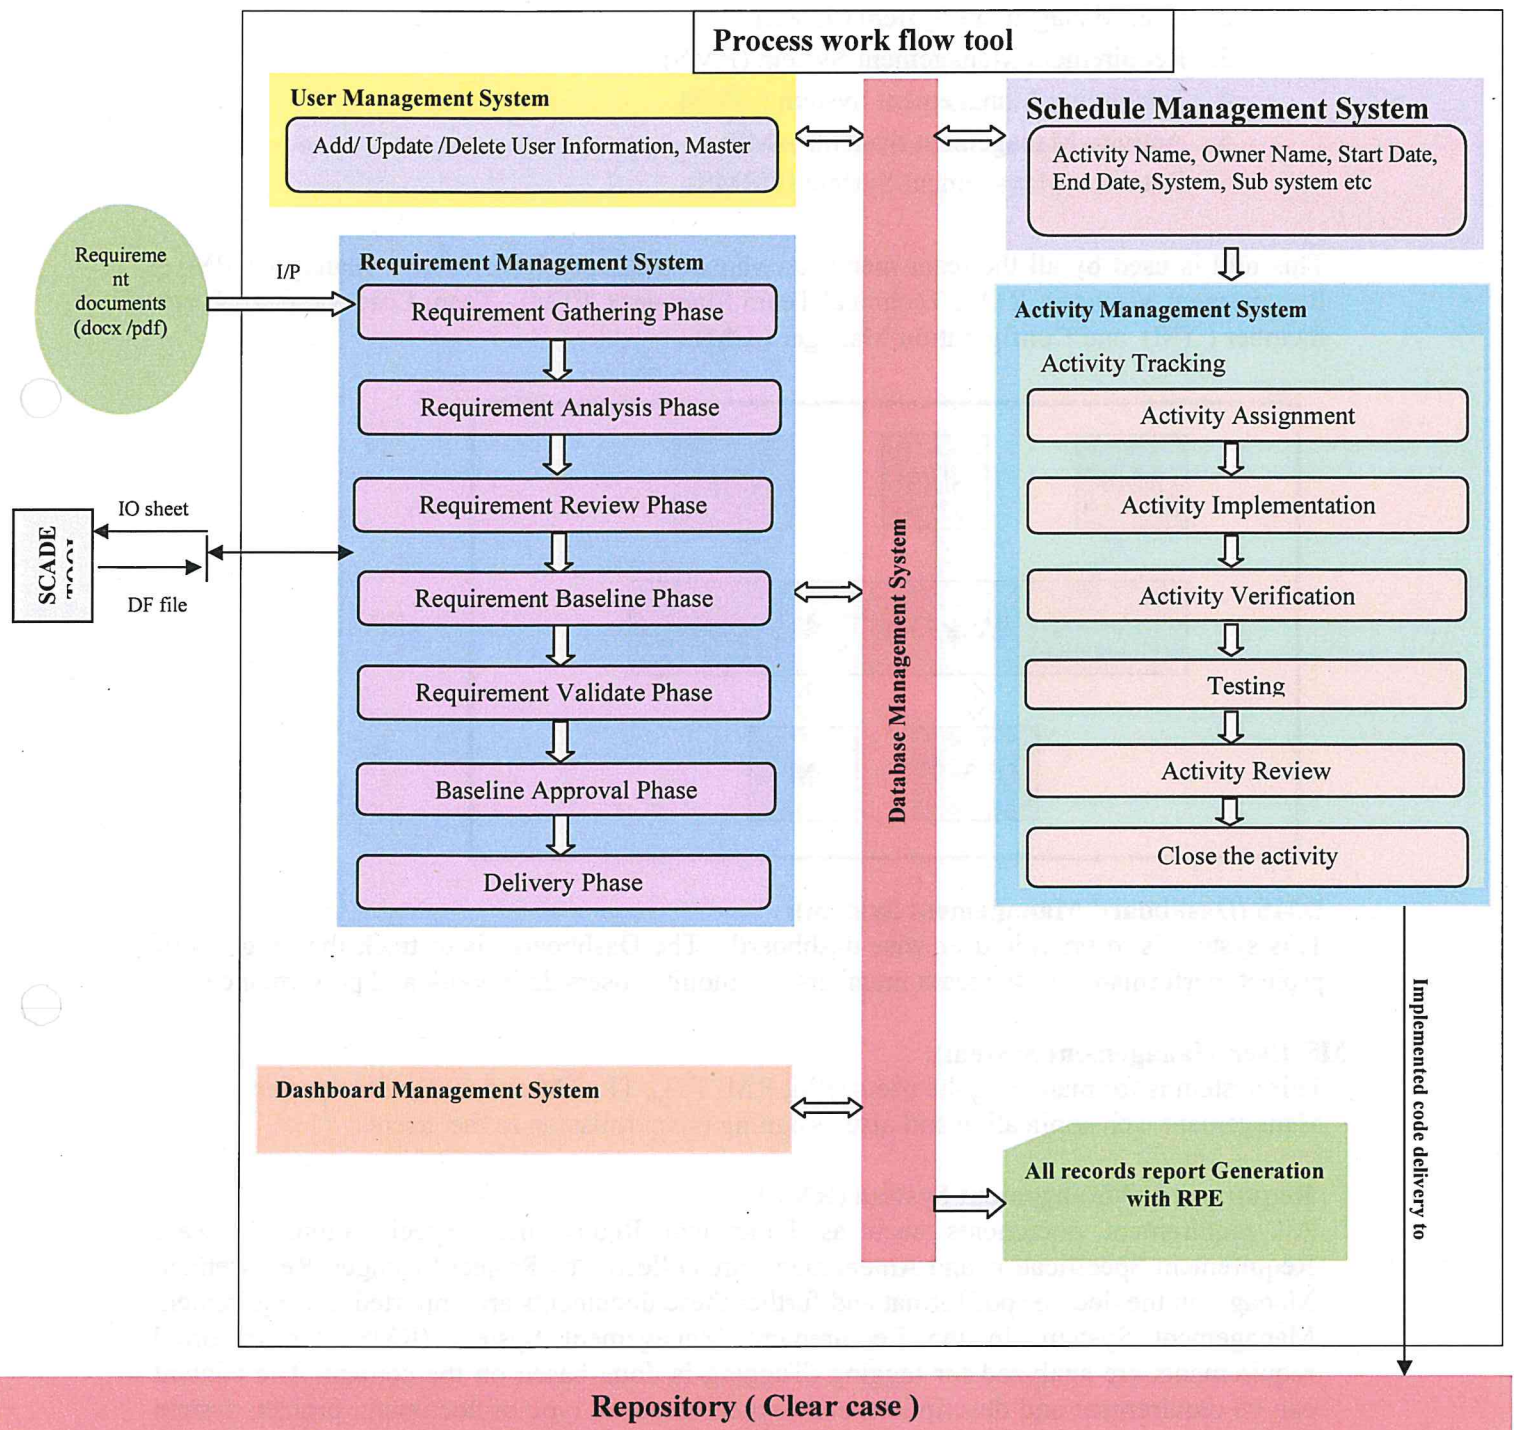

The process management web application is for managing all the SDLC phases of the project. It is sub divided into following sub modules:

1. Dashboard Management System (DMS)
2. User Management System (UMS)
3. Requirement Management System (RMS)
4. Scheduling Management System (SMS)
5. Activity Management System(AMS)
6. Database Management System (DBMS)

This tool is used by all the team members whose roles vary from Project Manager (PM) , Requirement Manager(RM) , Technical Team Manager (TTM) , Team Leader (TL) , Team member (TM) and Configuration Manager (CM) .

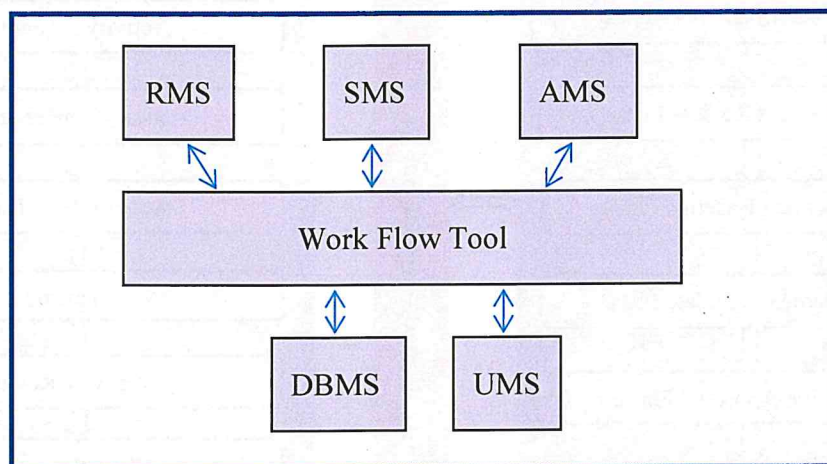

DMS (Dashboard Management System):

This system is to provide user wise dashboards. The Dashboard is to track the progress of project, performance of the team members. To monitor users daily work and performance.

UMS(User Management System):

This system is for managing the users (PM, RM, TTM, TL, TM and CM) of the project Management web application and also assigning the permission to the users.

Requirement Management System (RMS):

All requirement documents such as Functional Requirement Specification, Software Requirement Specification and Amendments are collected by Project Manager/ Requirement Manager in the docx or pdf format and further these documents are imported to Requirement Management System. In the Requirement Management System (RMS) the imported requirements are analyzed for tagging (Tagging is done based on the content. The content can be requirement and description) and tagged based on type of document, project, system and sub system and the unique number is generated. For each requirements then affected attributes such as requirement attributes, system and subsystem are updated. Those requirements are reviewed and approved by Change control Board (The CCB members are PM, RM, TTM, TL). The approved requirements are assigned to Requirement Manager to

Signature

check any display change / interface change / timing change and for those changes creating new/ update the existing Display page, IO Files.

Schedule Management System (SMS):

All the approved requirements are scheduled and converted as activities in Schedule Management System (SMS). The different types of phases in Schedule Management System are scheduling and assignment to the tasks to Team Leaders. In Activity scheduling phase Technical Team Manager will assign the approved requirements as Activities. The activities are scheduled and Assigned to respective CSCI Technical team Managers (TTM). The Microsoft Project Plan (MPP) is used for configuring the task schedule.


Activity Management System (AMS):

The different types of phases in Activity Management System (AMS) are breaking of main tasks into child tasks, assignment of tasks to team members (TM), Implementation of the tasks, validation by team leaders, Testing, Review of the work carried out and delivery of the verified code to the common repository.

The Activity Management has different record types and workflows to manage the tasks.

In Activity Assignment phase, the Team Leader (TL) will check the activities and prepare checklist for each task and if the task needs more resource then task shall be divided as child tasks and then assign to Team Members (TM's) with deadline. In Activity Implementation phase the TM will Implement the activity within deadline and fill the checklist and submits to Team Leader. If the Implementation time exceeds the deadline then activity will get freeze and task sent back to Team Leader. Team Leader will reassign the activity with remarks. If the task get reassigned the reassigned count also need for TM performance towards activity. In activity Verification phase the Team Leader will verify the checklist. If the implementation is satisfied the activity is assigned for L1 testing. After completion of the L1 testing, again team member submits the test result to team leader. If the Development and L1 Testing is completed then the Team Leader will deliver the implemented code to the main repository. Clear Case is used for version controller. All the workflow user will have access to the repository depends upon the project.

The Team Leader will submit this task to Technical Team Manager for Verification and Review with deliver details and checklist details. If the implementation/ testing are not satisfied TL can reassign the activity with remarks. Then development and testing should be done once again till the requirement gets satisfied. If the implementation/ testing satisfied the task will be assigned for L2 Testing. The TL assigns this task with description to TM. The TM will do the L2 Testing and will fill the test results and send s back to the TL. The TL will verify the L2 Tested task and submit task to the TTM. The TTM verify this Task and assign the task for Integration Testing (L3 testing). The L3 Tester should check the delivered code according to requirement and fill the test results and submits the Task to the TTM. If the Task satisfies the requirement then the TTM will close the task and send the Task to PM. If the Task not Satisfactory the same process should be done till the task satisfy the requirement.



If developed and tested tasks need test-case. The Test-case should be prepared for the tasks accordingly using Test-case record type. The test-case can be linked with task and approved requirements.

Database Management system(DBMS) :

The Database Management system(DBMS) is to store the data of workflow tool in an organized way.

Integration with other tools:

The tool is integrated with third party tools namely IBM clear case for version management, IBM Rational publishing engine (RPE) for report generation.

More details regarding the implementation of workflows and database would be provided during the project execution phase.

5. Features to be implemented in the existing tool

The following features are planned to be implemented in the existing tool:


5.1. Development of Word equivalent editor and integration with the existing tool

New web based interface to be developed for requirements collaboration. The interface should have the following features:

1. Provision to import requirement documents into the tool. Supported formats are .doc and .docx
2. Section based requirements tagging
3. Add/Update/Delete requirements manually
4. Provision to add/update requirements attributes
5. Multi user interactive comment management
6. Provision to view the history of comments, requirements and attributes
7. Export option to save updated requirements in word/pdf format

All the data related to the requirements shall be stored in the centralized database.

5.2. Development of new workflows for HMI requirement capture

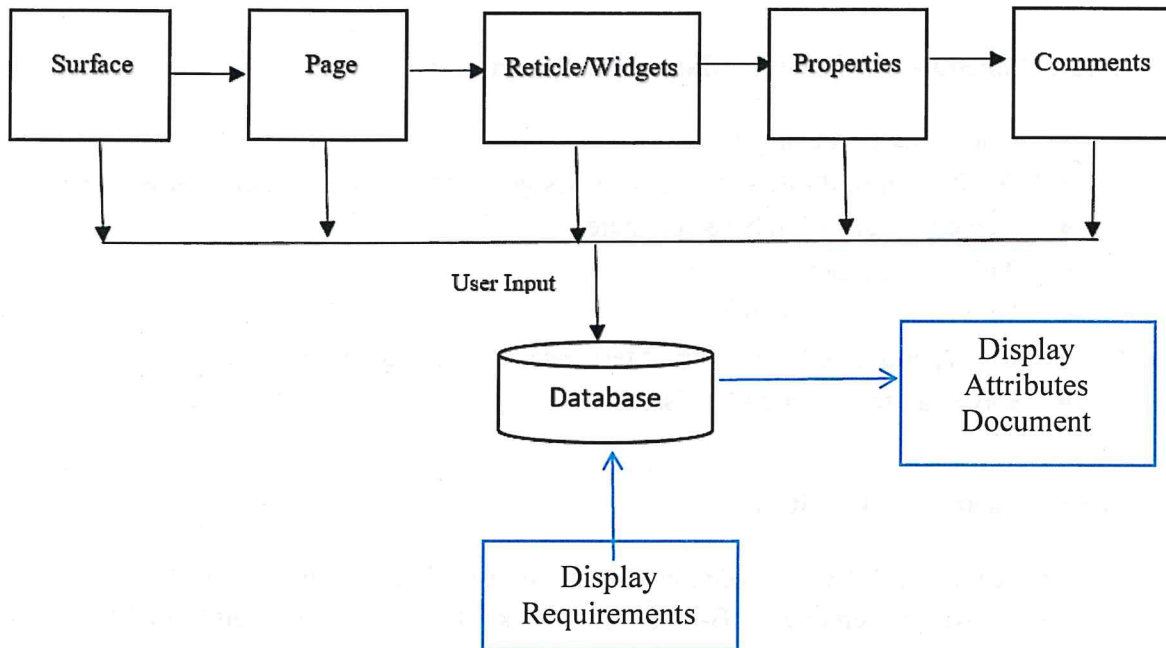

- Shall have option to link the display related requirements related to the new/ existing interface
- Shall have option to import/ export display related interface data to/from the work flow tool against particular version and project
- Shall have option to convert the SGFX data(ARIN 661 standard) to/from SVG
- Shall have GUI to view / edit / delete the display information w.r.t each page against particular version and project
- Shall be able to generate display Attributes document for one page/ multiple pages/ all pages against user selection of particular version and project
- Shall develop a work flow for the above

5.3. Support and maintenance of the existing work flow

Vendor shall carry out the following support and maintenance activities for the existing work flow.

5.3.1. Requirement Management Activities

- Creation of project and it mapped with system, subsystem and version.
- Resolving issues related to requirement tagging and requirement attributes
- Resolving issues related to linking of requirements

Signature

- Assigning requirements to different user for review/approve
- Issues observed during baseline of the requirements
- Solve day-to-day end user issues

5.3.2. Schedule and Activity Management Activities

- Scheduling task using MPP
- Handling of multiple states such as assign, open, resolve, frozen, re-assign etc.
- Check list validation based on states
- Daily status report preparation
- Activity history monitoring
- Issues pertaining to creation of test case and linking with requirement
- Solve day-to-day end user issues

5.3.3. ClearCase Activities

- Creation of VOB's (versioned object base) and views, change VOB ownership, move and remove VOB- checkin / checkout using a view, change VOB elements.
- Permissions and importing elements into VOB.
- Administrating the importing elements into VOB.
- Handling clearcase regions and clearcase registries.
- Data management –VOB storage pools, registry files.
- Planning for up gradation of clearcase version in sever as well as client.
- Branch creation and config spec edition according to team leader requirement and performing the operations like moving, recreation, views and VOB's.
- Implementation of script for Add to source control recursively, checkin-checkout recursively, automates the backup process and generates license info report.
- Writing and attaching triggers to VOB's elements according to requirements.
- Knowledge about configuration management & clearcase commands for efficient work with rational clearcase and other tools.
- Implementation of base level and UCM level VOBs
- Access permissions to team members and leaders to VOBs depending on project team and role

5.3.4. RPE Activities

- Create project specific custom report templates in RPE in line with DO-2167A DO-178 as provided by ADA.

- Documentation and configuration control of templates implemented
- Prepare and maintain document for user guidance
- Generate report from workflow with the help of existing templates as well as new templates based on the project.
- Solve day-to-day end user issues
- The reports will be generated as per the following schedule
 - Daily uptime reports
 - Weekly uptime reports
 - Fortnightly uptime reports
 - Quarterly uptime reports

5.3.5. User Management Activities

- New/edit/delete user account creation
- Authorization and permissions to all developers according to projects and Task.
- Training all the project teams, administrator regarding workflow, IBM clear case and RPE tool operations and implementations

5.3.6. Server Activities

- Manage tool licenses
- Monitor the VOB health and reporting
- Monitor the server health and reporting
- Migration of tool to another VM in case of server upgradation
- Migration of CC and RPE licenses to another VM in case of server upgradation

5.3.7. Backup and Restoration Activities

- Backup of VOB repositories.
- Back up of the project data on weekly and monthly basis.
- Restoration checks for the project data on monthly basis.

5.3.8. Miscellaneous Activities


- Installation, configuration related to workflow
- Issues related to document generation through tool
- Troubleshooting errors.



- Resolve issues related to day-to-day activity of during merging of the versioned code
- Configuration of the use authorizations in the server for individual team members.
- Preparing tools manuals & trouble shooting document and regularly updating and maintaining.
- Overall responsibility for applications uptime, operations user issues resolution and effectiveness in usage of tools.

6. Proposed architecture

The system shall be developed in Micro-Service based architecture for all the modules in the workflow tool as given below. The detailed implementation architecture shall be prepared by the vendor and presented during the Technical Evaluation. The actual project implementation plan shall be designed and mutually agreed upon during project execution phase.

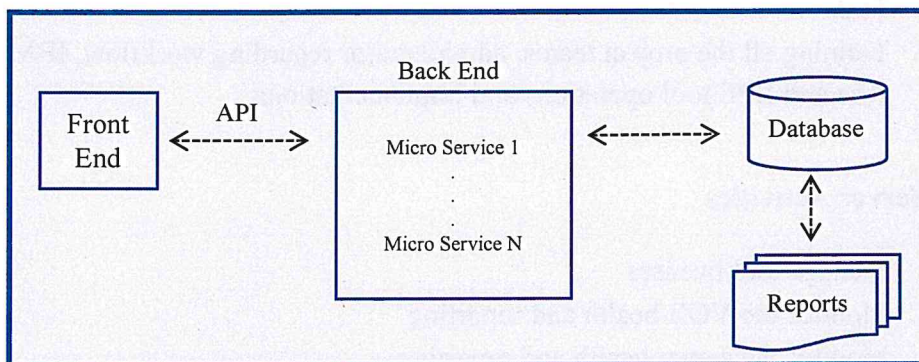

The following technologies are suggested for the project implementation:

Front End: Angular / React

Back End: JAVA, Spring Boot, Micro Service, Socket IO

Database: MongoDB or any NoSQL DB

Deployment: Docker, Kubernetes or any other open source deployment tool

Note: Only open source software and libraries shall be used for development and deployment


The following micro-services shall be developed for back end:

- Requirement Service
- Traceability Service
- Baseline Service
- Comparison Service
- Dashboard Service
- Test Case Service
- Activity Service

Signature

- Repository Service
- History Service
- Document Service
- Report Service

The micro services shall be created in order to support Docker&Kubernetes architecture which will be provided by ADA for integration. The deployment architecture schematic is given below.

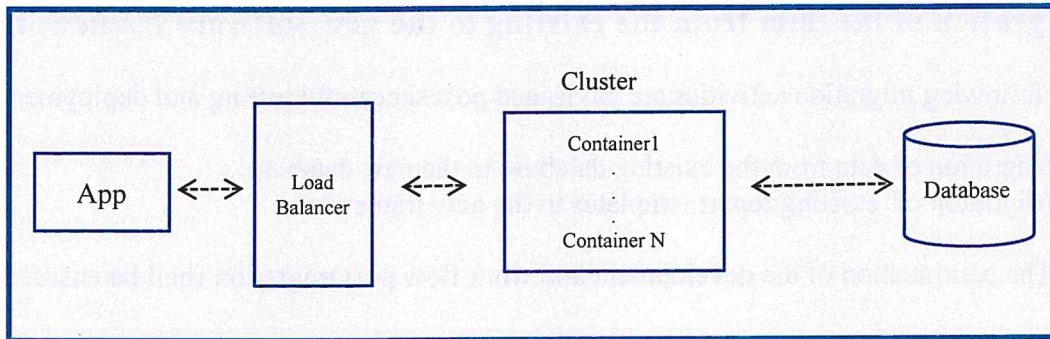

7. Activities to be carried for new software framework implementation

Vendor shall carry out the following activities for new software implementation.

7.1.Design and development of tool with new software framework

The following features and workflows available in the existing tool need to be re-developed in the new proposed software architecture:

- a. User Management System
- b. Dashboard ManagementSystem
- c. Project Management System
- d. Requirement Management System
- e. Scheduling Management System
- f. Activity Management System
- g. Database Management System
- h. Integration with Clear Case
- i. Integration with RPE for report generation

7.2.Testing and Documentation with new software framework

The following tests shall be carried out in a test environment:

- a. Unit Test
- b. Functionality Test
- c. Database Test
- d. Performance Test
- e. Load Test needs to be carried out for minimum of 500 users

Signature

The following documentation shall be generated:

- a. Database Design document
- b. Software Architecture and design document
- c. Software Test Document
- d. User Manual

7.3. Migration of the data from the existing to the new software framework

The following migration activities are envisaged post successful testing and deployment:

- a. Migration of data from the existing database to the new database.
- b. Migration of existing report templates to the new framework

The continuation of the development and work flow post migration shall be ensured.

7.4. SCADE and RAPSODY integration

SCADE and RAPSODY tools shall be integrated with the new tool

7.5. Support and maintenance of the work flow

Vendor shall carry out the following support and maintenance activities for the new work flow.

7.5.1.1. Requirement Management Activities

- Creation of project and it mapped with system, subsystem and version.
- Resolving issues related to requirement tagging and requirement attributes
- Resolving issues related to linking of requirements
- Assigning requirements to different user for review/approve
- Issues observed during baseline of the requirements
- Solve day-to-day end user issues

7.5.1.2. Schedule and Activity Management Activities

- Scheduling task using MPP
- Handling of multiple states such as assign, open, resolve, frozen, re-assign etc.
- Check list validation based on states
- Daily status report preparation
- Activity history monitoring
- Issues pertaining to creation of test case and linking with requirement
- Solve day-to-day end user issues



7.5.1.3. ClearCase Activities

- Creation of VOB's (versioned object base) and views, change VOB ownership, move and remove VOB- checkin / checkout using a view, change VOB elements.
- Permissions and importing elements into VOB.
- Administrating the importing elements into VOB.
- Handling clearcase regions and clearcase registries.
- Data management –VOB storage pools, registry files.
- Planning for up gradation of clearcase version in sever as well as client.
- Branch creation and config spec edition according to team leader requirement and performing the operations like moving, recreation, views and VOB's.
- Implementation of script for Add to source control recursively, checkin-checkout recursively, automates the backup process and generates license info report.
- Writing and attaching triggers to VOB's elements according to requirements.
- Knowledge about configuration management & clearcase commands for efficient work with rational clearcase and other tools.
- Implementation of base level and UCM level VOBs
- Access permissions to team members and leaders to VOBs depending on project team and role

7.5.1.4. RPE Activities

- Create project specific custom report templates in RPE in line with DO-2167A DO-178 as provided by ADA
- Documentation and configuration control of templates implemented
- Prepare and maintain document for user guidance
- Generate report from workflow with the help of existing templates as well as new templates based on the project.
- Solve day-to-day end user issues
- The reports will be generated as per the following schedule
 - Daily uptime reports
 - Weekly uptime reports
 - Fortnightly uptime reports
 - Quarterly uptime reports

Inte

7.5.1.5.User Management Activities

- New/edit/delete user account creation
- Authorization and permissions to all developers according to projects and Task.
- Training all the project teams, administrator regarding workflow, IBM clear case and RPE tool operations and implementations

7.5.1.6.Server Activities

- Manage tool licenses
- Monitor the VOB health and reporting
- Monitor the server health and reporting
- Migration of tool to another VM in case of server upgradation
- Migration of CC and RPE licenses to another VM in case of server upgradation

7.5.1.7.Backup and Restoration Activities


- Backup of VOB repositories.
- Back up of the project data on weekly and monthly basis.
- Restoration checks for the project data on monthly basis.

7.5.1.8.Miscellaneous Activities

- Installation, configuration related to workflow
- Issues related to document generation through tool
- Troubleshooting errors.
- Resolve issues related to day-to-day activity of during merging of the versioned code
- Configuration of the use authorizations in the server for individual team members.
- Preparing tools manuals & trouble shooting document and regularly updating and maintaining.
- Overall responsibility for applications uptime, operations user issues resolution and effectiveness in usage of tools.

8. Onsite support

Vendor shall deploy resources at ADA / Vendor's site to carry out the above activities to meet the milestones under the supervision of a technical Manager from the vendor side.




However the maintenance and integration activities need to be carried out by resident resources deployed by vendor at ADA. In order to realize the activities agreed for each milestone, tasks to be scheduled monthly wise in concurrence with technical manager and monitored daily wise.

9. Material to Be Given by ADA

- Access to Servers, client PCs, network switches and necessary hardware for carrying out the activities at ADA premises
- Access to Clear case and RPE software
- Deployment framework for the new software

10. Vendor - Pre-requisite Qualification

1. Vendor shall carry out the activities at ADA/Vendor's site as per SOW.
2. ISO 9000 certification would be considered desirable.
- ✓ 3. Vendor shall not subcontract the project.
- ✓ 4. Supplier's expertise in the following areas of each category would be evaluated by the Acquirer. During technical evaluation, vendor shall demonstrate the technical know-how and skills as per the document attached as Annexure- A.
 - a. Word equivalent editor integration to web tool
 - b. Web based tool development using PHP / Angular / React
 - c. Work flow development for embedded / simulated SDLC
 - d. Process work flow implementation
 - e. IBM tools based configuration control and Report Generation
 - f. Database structure design and migration
 - g. Test case/ Test scenario generation and automation
 - h. Dockers , Container and KUBERNETES based deployment
 - i. Micro services based applications
- ✓ 5. Vendor's project team should have executed successfully minimum of 4 different projects in the above domain areas with each project span of minimum 6 months. The vendor shall submit the proof for the same along with technical bid mentioning PO details, the nature of the work carried out as per Annexure –B.1 and Annexure – B.2.
6. Environment required for executing the project shall be provided by ADA



- ✓7. All items developed by vendor under this project are proprietary of ADA and shall not be disclosed and vendor does not have any rights on the software/artifacts developed.
- 8. Periodical project review shall be conducted with the vendor at least once in a month
- 9. A dedicated team Leader/ single point of contact shall be deployed for the project.
- 10. Resource plan shall address attrition risk of the firm.
- 11. All artifacts developed during the project lifecycle shall be submitted to ADA with source code and documentations at appropriate stages
- ✓12. Vendor shall sign Non-DISCLOSURE Agreement with ADA.
- 13. Vendor shall maintain highest level security for the items developed and for the development environment for this project.

11. Technical Team Expertise

The requisite qualification and experience required for the deployed resources are given below. The vendor shall provide resource compliance as per Annexure C for all the resources whom they are planning to deploy for this work.

Signature

Team Leader Pre Requisite Qualification and Experience

ME/ BE in Computer science/ Electronics/ Instrumentation/ Avionics/ Aeronautics with Experience of 7+ years in the relevant domain area.

Team Leader should have knowledge in each category listed below:

Tools and database: My SQL, NoSQL, Clear case (Ver 9.x) , IBM RPE (ver 6.x) , Active directory, LDAP, DB 2 (10.x), Dockers, KUBERNETES-- minimum 5 areas

Technical Skills : JAVA,Java Spring boot,Socket IO ,Angular,React, C#, Java Script , JQuery, HTML, Bootstrap, Python, PHP, AJAX, Rest API, Perl, VB script-- minimum 5 areas

Operating System: Windows 64 bit, LINUX 64 bit, UBUNTU 64 bit, MAC , Windows servers -- minimum 2 areas

Hardware knowledge: Servers, VMs, Storage devices-- Desirable

Team Member Pre Requisite Qualification and Experience

ME/BE/MCA/MSc in Computer science/ Electronics/Avionics/ Aeronautics should have Experience of 4+ years in the relevant domain area.

Team member should have knowledge in each category listed below:

Tools and database : My SQL, NoSQL, Clear case (Ver 9.x) , IBM RPE (ver 6.x) , Active directory, LDAP, DB 2 (10.x), Dockers, KUBERNETES -- minimum 3 areas

Technical Skills : JAVA,Java Spring boot,Socket IO ,Angular,React, C#, Java Script , JQuery, HTML, Bootstrap, Python, PHP, AJAX, Rest API, Perl, VB script -- minimum 3 areas

Operating System: Windows 64 bit, LINUX 64 bit, UBUNTU 64 bit, MAC , Windows servers -- minimum 1 area

Hardware knowledge: Servers, VMs, Storage devices – Desirable

12. Technical evaluation

- ✓a) During technical evaluation, vendor shall demonstrate the technical know-how and skills as per the document attached as Annexure- A.
- ✓b) The detailed implementation architecture for the new software frame work shall be prepared by the vendor and presented during the Technical Evaluation
- ✓c) The vendor shall submit the proof of experience as per Annexure -B

- ✓d) The vendor shall submit the resumes of their regular employees along with technical bid whom they are planning deploy for this project that has experience and knowledge as per section 11 along with resource compliance as per Annexure –C.
- ✓e) TEC committee will be evaluating the capability of the vendor based on technical demonstration, the vendor's experience on executing similar projects and the resource's experience. In case, TEC found the resumes submitted is not as per SOW, the vendor needs to submit alternate resumes as per SOW within a weeks' time.
- ✓f) Vendor shall provide the confirmation for their willingness to deploy at least 2/3rd of the resources which are found suitable by the TEC committee during the evaluation if PO is placed. In case, it is found that the vendor is not complying the same, ADA is having rights to terminate the PO.

13. Resource deployment


- i. All the resources shall be deployed at once so that the training would be imparted by ADA in one short within one month of PO placement.
- ii. Minimum two resources should be available at ADA for carrying out the upgrade, maintenance and testing activities
- iii. Vendor shall deploy the other resources at Vendor's site or/and at ADA for the development activities. However the integration, migration and testing activities shall be carried out at ADA.
- iv. Vendor shall submit the documents for the resources identified as per PO within one months' time from the placement of PO as per Annexure D.
- v. In case, during resource screening it is found that the resumes submitted by the vendor is not complying the SOW, ADA is having rights to terminate the PO.
- vi. Period of resource deployment is not considered for the payment.
- vii. After the resource deployment period, T0 of the project will be started

14. Training

- 1. One time Training (about 30 days) would be imparted by ADA to make the Vendor Team understand /familiarize Project, Process, and System after the deployment of resources.
- 2. To take full advantage of this privilege, the vendor shall place entire Team (intended for the work at ADA) at once.
- 3. At a later stage, it shall be whole and sole responsibility of vendor to train any new resources.
- 4. Supplier shall make necessary process/procedure document/templates to ensure smooth execution of activities.

15. Handing over activities

- a) The vendor shall provide knowledge transfer to ADA in the last milestone of the PO
- b) During this time, vendor shall address any performance related issues for the already developed databases and visualization software.



- c) The vendor shall make necessary documents and procedures and obtain approval from the project coordinator.
- d) Based on the completion of the above performance satisfactory report will be approved by the project coordinator.

16. Schedule and Milestone Deliverables

Projector Coordinator approved copies of the Milestone Completion report shall be submitted for each milestone.

Project timeline with the proposed milestones (in calendar months) is shown below for each quarter: 2 Builds in existing Workflow, 3 Builds for new Workflow are envisaged.

T0: Completion of the resource deployment, Training. Approximately 1 month is estimated for the completion for resource deployment & training.

Milestone	Deliverables	Time Line
1	a) Build-No: 1 Delivery of existing workflow as per section 5.1 b) Requirement Analysis for new workflow as per section 5.2 c) Project Implementation Plan for the new workflow framework as per section 6 d) SRS, SDD and Test Case documents as per section 6 e) Wireframe finalization with prototypes for new workflow as per section 6 f) Support for the existing work flow as per section 5.3	T0 + 3 months : T1
2	a) Build-No:2 Delivery of existing workflow as per section 5.2 b) Support for the existing work flow as per section 5.3 c) Build-No: 1 – New Workflow: ➤ UI Screens for all the requirements as per section 6	T1 + 3 months : T2
3	a) Build-No: 2 – New Workflow: ➤ User Management System as per section 7.1 ➤ Project Management System as per section 7.1 ➤ Requirement Management System as per section 7.1 ➤ Scheduling Management System as per section 7.1 ➤ Database Management System as per section 7.1 ➤ Database migration w.r.t above modules as per section 7.1 ➤ Integration with RPE for report generation as per section 7.1 ➤ Test Reports w.r.t Build as per section 7.2 b) Support for the work flows as per section 7.5	T2 + 3 months : T3

Signature

Milestone	Deliverables	Time Line
4	a) Build-No:3 – New Workflow: ➤ Activity Management System as per section 7.1 ➤ Dashboard Management System as per section 7.1 ➤ Database migration w.r.t above modules as per section 7.1 ➤ Integration with Clear Case as per section 7.1 ➤ SCADE and RAPSODY integration as per section 7.4 ➤ Testing and Documentation as per section 7.2 ➤ Test Reports w.r.t Build as per section 7.2 b) Support for the work flows as per section 7.5 c) Handing over activities report as per section 15	T3 + 3 months : T4

17. Acceptance criteria

- a) ADA project coordinator shall review the progress made by the supplier on the work assigned in the presence of project coordinator from supplier side for every mile stone.
- b) For each defined mile stone the completion report shall be generated by the supplier duly approved by project coordinator of Acquirer.
- c) The approved mile stone report shall be submitted along with deliverables for payment.
- d) Payment shall be made mile stone based as follows:

Mile stone number	% of PO
Mile Stone 1	25
Mile Stone 2	25
Mile Stone 3	25
Mile Stone 4	25
Total	100

- In case if there is delay in completion of the mile stones, the vendor has to complete the same without additional cost.

18. Terms & Conditions

- This Service Contract is for a period of oneyear.
- Shall deploy minimum 6 resources including a dedicated team Leader/ single point of contact for the project
- Pre-bidding meeting will be conducted within 2 weeks time from the date of enquiry floated.
- Security procedures of ADA shall be followed for all the deployed resources while joining and resigning.
- Vendor shall deliver the manpower services who are on the permanent roles of the company with sincerity and by maintaining confidentiality.
- Police verification letter to be obtained for the deployed resources before executing the work.
- Confidential agreement (NDA) to be signed by the vendor.

- The working schedule shall be as per ADA norms.
- Vendor shall ensure scheduling of usage of resources and ensuring that absence and attrition does not affect the deliverables.
- If deployed resource found un-satisfactory, ADA has right to demand to depute another suitable person.

Inte

Annexure A: Activities for Demonstration during Technical Evaluation

1. Objective:

To assess the expertise of the vendor and the resources planned to be deployed by the vendor through technical demonstration.

2. POC areas

ADA would define problem statement during technical evaluation stage in the following areas:

- a. Word equivalent editor integration to web tool
- b. Offline Setting up of Docker Container and KUBERNETES based deployment and demonstration with sample micro services
- c. Understanding of Auto scaling of micro services architecture shall be provided
- d. Sample integration of third part tool to a web tool

Vendor shall prepare the technical solution and demonstrate within two weeks' time from the day the problem is shared. Non demonstration / non satisfaction of the technical demo within stipulated time would lead to rejection of the technical bid.

3. Description of Activities

- a) Implement the solution based on the problem statements provided by ADA .
- b) During the evaluation, all the project files would be submitted to ADA in Soft copy form on non-returnable basis


4. Pre-bid meeting

During the Pre-bidding meeting , the vendor shall intimate ADA regarding the environment to be made ready at ADA for technical evaluation.



Annexure –B.1:CompanyExperience Details Template

S. No	Technical areas as per SOW	PO description with details of work carried out	Reference PO	PO relevance w.r.t ADA SOW section No	No of resources deployed for the PO
1					
2					
3					
4					
5					
6					
7					
8					



Annexure –B.2: CompanyDetails Template

Sl.no	Parameter	Information
1.	Year of Establishment of Company	
2	Total employee strength in India	
3	Years of experience in the relevant domains demanded by SOW and the tools used	
	Workflow Software development	Years : Tools:
	Web based software development	Years : Tools:
	Databases design and development	Years : Tools:
	Test case scenario tool design and development	Years : Tools:
	IBM tools Integration	Years : Tools:
	Containerization	Years : Tools:
	Certification	Years : Tools:
	Any Other Areas	Years : Tools:
4.	Total employees currently working in the company with relevant experience demanded by SOW	
5.	Mitigation Plan for the milestone completion	

Smile

Annexure –C: Experience Compliance Matrix for the Resources planned to be deployed by the vendor

Sl. no	Section no of SOW	Requirement	Information
1.		Name of the resource	
2.		No of Years / months of experience in vendor's firm	
3.		Qualification	
4.		Academic records	
5.		Experience	Project name : Name of the project Works carried out : Description of the work carried out by the resource for the project No of years / months worked in the project:
6.		The resources should have knowledge in the below listed areas in each category and the same would be evaluated by the Acquirer during TEC	
		Tools and databases	Projects handled with this area:
		Technical skills	Projects handled with this area:
		Operating System	Projects handled with this area:
		Any Other Areas	



Annexure –D: Resource screening requirements to be complied by the vendor after PO is placed

1. Personal deployed to ADA needs to be regular employees of the vendor. Proof of the same may be submitted as per PO terms.
2. The details of the personal likely to be deployed to ADA were provided by during the Technical evaluation based on which the firm was technically qualified. Vendor needs to submit the resumes and the following documents for those personnel :
 - a. Resume of the person
 - b. Documents as proof of their education qualification as per SOW
 - c. Documents as proof of their experience certificate covering relevant experience as per SOW.
3. Documents pertaining to ADA security/admin clearance.
4. Documents pertaining to ADA IT compliance/undertaking.
5. NDA in the prescribed format as per SOW
